


**FORSYTH COUNTY SCHOOLS 2014 CAPITAL PROGRAM TIMELINE**

LOCATION	CONSTRUCTION PROJECT	ARCHITECT	A/E START	GC/CM	OPEN	SUMMARY STATUS
<b>HIGH SCHOOL ADDITIONS AND MODIFICATIONS</b>						
<b>North Forsyth H.S.</b>	Stadium visitors concession and restroom	BRPH	Done	Charles Black	Done	Certificate of Occupancy issued 8/14/14
	Gymnasium and Cafeteria	FSF	Done	Barton Malow	Aug-16	sitework , utilities, foundations in progress
	Additions	FSF	Done	Barton Malow	Aug-16	
	Renovations	FSF	Done	Barton Malow	Aug-17	
<b>Forsyth Central H.S.</b>	Additions	CPL	Done	Parrish	Aug-16	sitework , foundations, masonry , steel in progress
	Renovations	CPL	Done	Parrish	Aug-17	
<b>South Forsyth H.S.</b>	Gymnasium and Cafeteria	MSSA	Done	Balfour Beatty	Aug-16	sitework , foundations, masonry , steel in progress
	Additions	MSSA	Done	Balfour Beatty	Aug-16	
	Renovations	MSSA	Done	Balfour Beatty	Aug-17	
<b>Lambert H.S.</b>	Additions- 19 classrooms , band	BRPH	Done	Charles Black	Aug-16	sitework , foundations, masonry , steel in progress
	Renovations	BRPH	Done	Charles Black	Aug-16	
	Artificial Turf Field (IGA \$ , not bond)	Breedlove	Done	Shaw	Oct-15	light towers installed, sitework & utilities in progress, turf mid Sept
<b>West Forsyth H.S.</b>	Additions - Performing Arts (Band,Choral)	BRPH	Started	Apr-16	Apr-17	WFHS stakeholder committee formed
	Renovations (Art,Computer Labs)	BRPH	Started	Apr-16	Aug-17	BRPH design started
<b>High School #7</b>	Land Purchase				Done	11/10/14 closed
<b>Denmark H.S.</b>	Denmark HS New Construction	BRPH	Started	Mar-16	Jun-18	GDOE \$ process 2015, design to be complete 2/2016



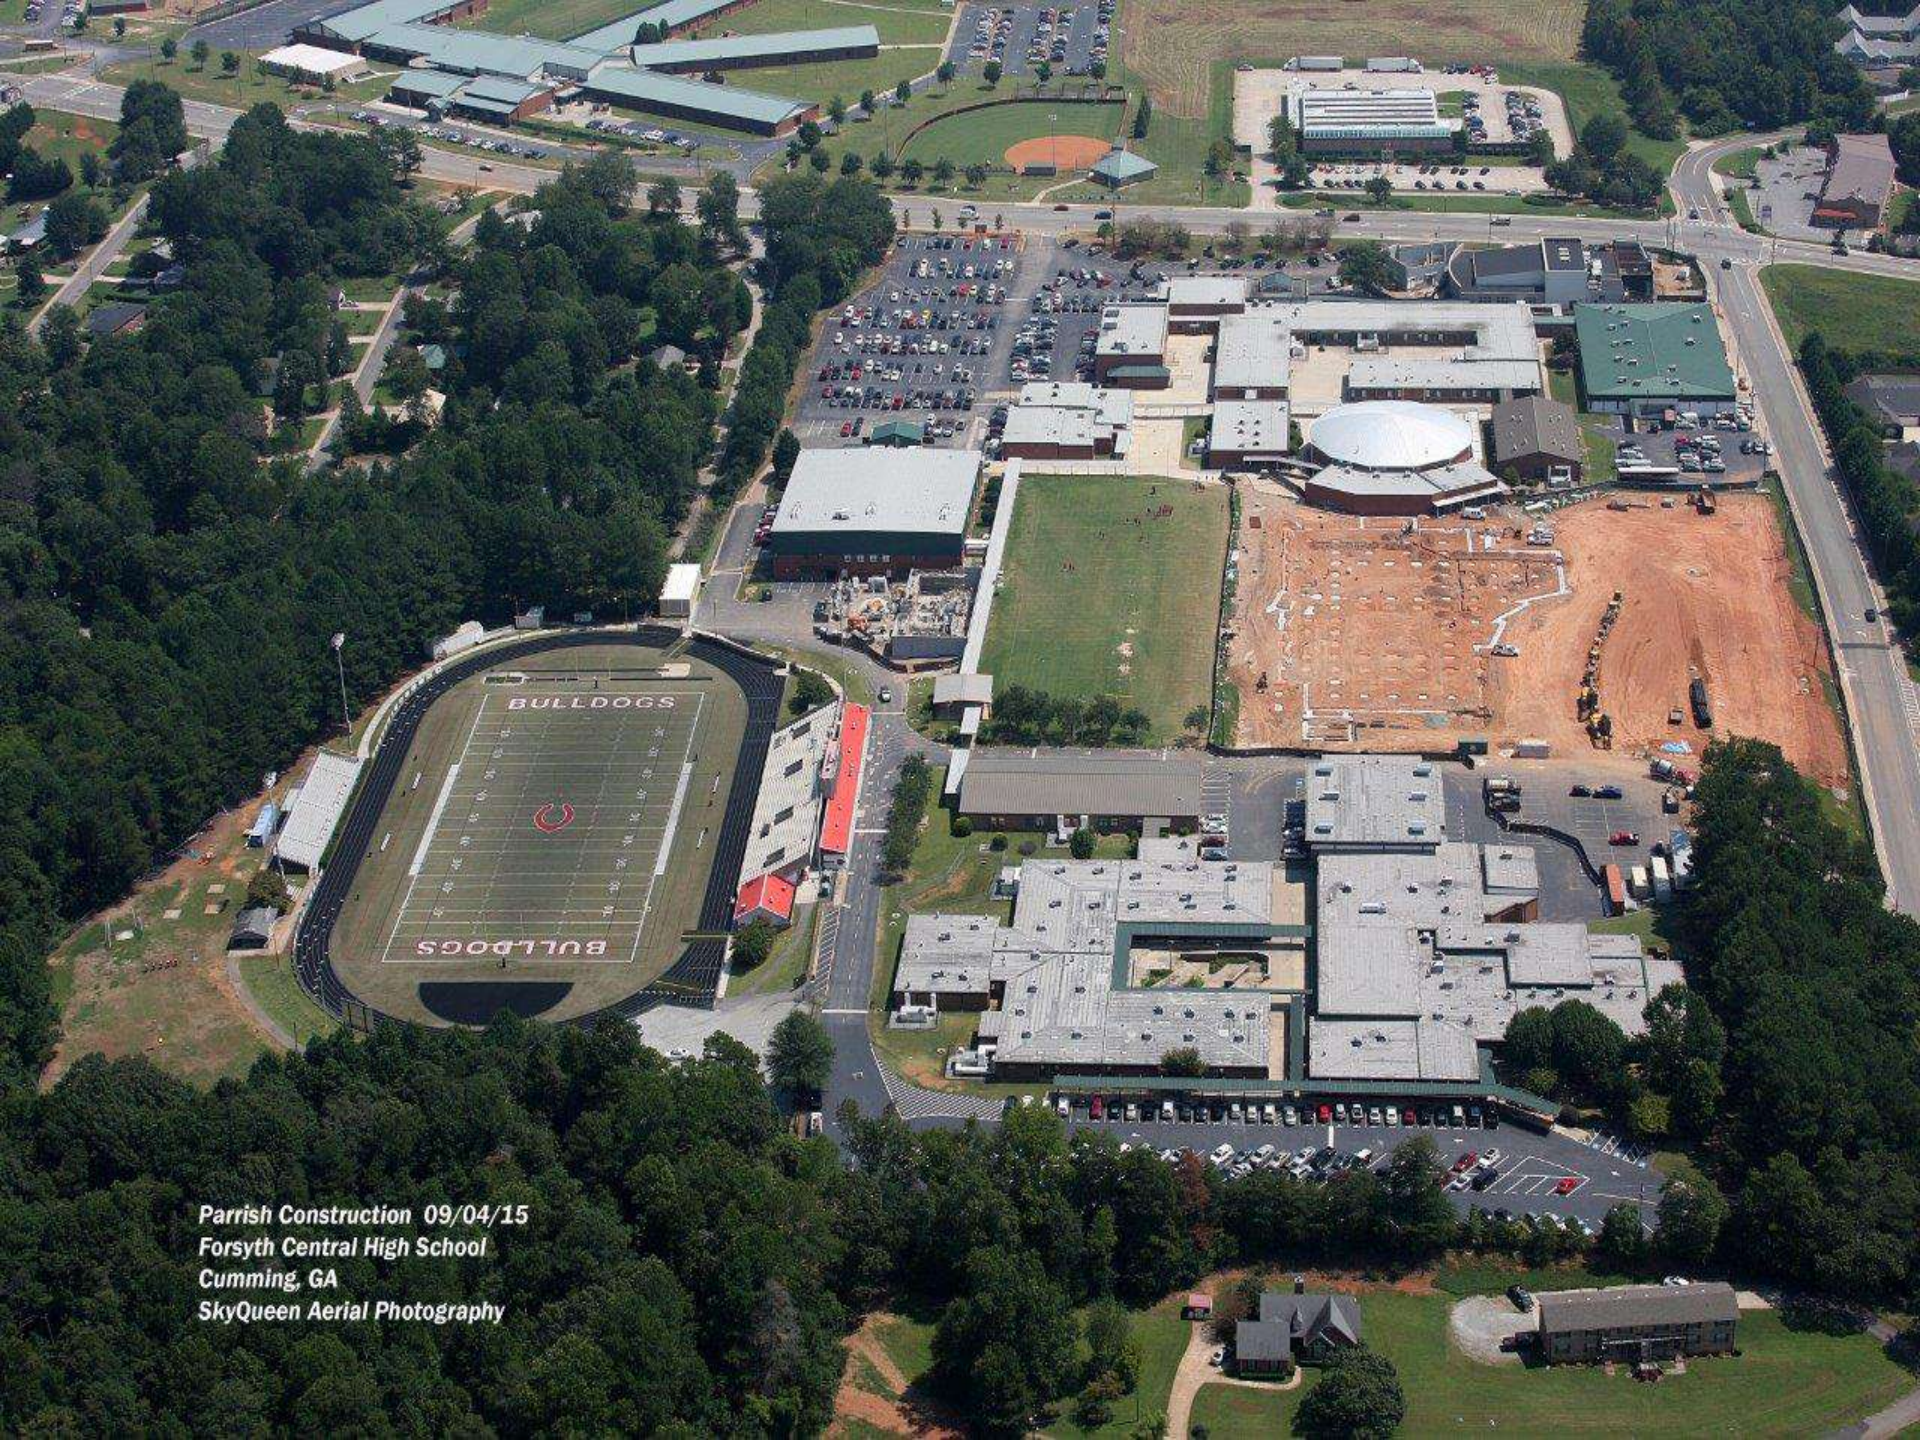

Parrish Construction 09/04/15  
Forsyth Central High School  
Cumming, GA  
SkyQueen Aerial Photography





*Lambert High School*

Print #150829085

Date: 08/29/15

Lat/Lon: 34.105773 -84.138922

Order No. 59776



Aerial Photography, Inc. 954-568-0484

**MIDDLE SCHOOL ADDITIONS AND MODIFICATIONS**

<b>Liberty M.S.</b>	Modify front entrance for security	James Buckley	Done	Done	Done	Complete
	Modifications for performing arts	James Buckley	Sep-15	Apr-16	Aug-17	Program / Design kick off meeting 8/26/15
	Expand Band Classroom	James Buckley	Sep-15	Apr-16	Aug-17	
<b>Little Mill M.S.</b>	Modify front entrance for security	James Buckley	Done	Done	Done	Complete
	Modify front drive entrance	McFarland Dyer	Sep-16	Mar-17	Aug-17	
<b>North Forsyth M.S.</b>	Modify front entrance for security	James Buckley	Done	Done	Done	Complete
	Media center , performing arts, team room	James Buckley	Sep-15	Apr-16	Aug-17	Program / Design kick off meeting 8/26/15
	HVAC replacement / modification	CGE	Done	Capital City	Aug-15	HVAC completed
<b>Otwell M.S.</b>	Modify front entrance for security	James Buckley	Done	Done	Done	Complete
	Expand technology lab , drama	James Buckley	Sep-15	Apr-16	Aug-17	Program / Design kick off meeting 8/26/15
<b>Piney Grove M.S.</b>	Modify front entrance for security	James Buckley	Done	Done	Done	Complete
	Front Drive sidewalk	McFarland Dyer	Sep-16	Mar-17	Aug-17	
	Modify technology lab	James Buckley	Sep-15	Apr-16	Aug-17	Program / Design kick off meeting 8/26/15
<b>South Forsyth M.S.</b>	Modify front entrance for security	James Buckley	Done	Done	Done	Complete
	23 Classroom Addition	James Buckley	Done	RaLin	Aug-16	sitework , utilities, foundations in progress
	Expand Media Ctr ,Cafeteria, Modify PA	James Buckley	Done	RaLin	Aug-16	
	HVAC replacement / modification	James Buckley	Done	RaLin	Aug-16	

<b>Riverwatch M.S.</b>	Modify front entrance for security	James Buckley	Done	Done	Done	Complete
	24 Classroom Addition	James Buckley	Done	RaLin	Aug-16	sitework , utilities, foundations in progress
	Expand band room	James Buckley	Done	RaLin	Aug-16	new field sodded
<b>Vickery Creek M.S.</b>	Modify front entrance for security	James Buckley	Done	Done	Done	Complete
	Expand Media Ctr , Technology Lab	James Buckley	Sep-15	Apr-16	Aug-17	Program / Design kick off meeting 8/26/15
	HVAC replacement / modification	CGE	Done	Capital City	Aug-15	HVAC completed
<b>Middle School #10</b>	MS #10 New Construction	James Buckley	Done	Evergreen	Aug-16	on schedule masonry, steel , roof, MEP rough, curbing in progress
<b>(DeSana Middle School)</b>						
<b>Middle School #11</b>	MS #11 land purchase					search, due dilligence options in progress



DESANA MIDDLE SCHOOL  
Alpharetta, Georgia

AUG 25 2015





# South Forsyth Middle School



Riverwatch Middle School

**ELEMENTARY SCHOOL ADDITIONS AND MODIFICATIONS**

<b>Brandywine ES</b>	Brandywine ES New Construction	LPBC	Done	Charles Black	Aug-16	on schedule masonry, steel , roof, MEP rough, curbing in progress
<b>Midway ES</b>	Sanitary sewer service	CEC	Started	Nov-16	Aug-16	Civil Engineer Consultants Inc design in progress
<b>Daves Creek</b>	HVAC replacement / modification	CGE	Done	Waters	Aug-15	HVAC substantially completed
<b>Settles Bridge</b>	HVAC replacement / modification	CGE	Done	Capital City	Aug-15	HVAC completed
<b>General</b>	security,media ctr, partitions, parking	TBD				



*Brandywine Elementary School*

Print #150829093

Date: 08/29/15

Lat/Lon: 34.131329 -84.248087

Order No. 49821



Aerial Photography, Inc. 954-568-0484
