

**CORONA-NORCO UNIFIED SCHOOL DISTRICT
MEASURE GG - CITIZENS' OVERSIGHT COMMITTEE**

Annual Organizational Meeting

August 24, 2020, 6:30 P.M.

Zoom Meeting

Citizens' Oversight Committee Members

Gregory Coker, Chair

Jami Merchant, Vice Chair

Nilo Ambriz
Kevin Bash
Raul Gomez
Bryan Graves

Corinne Holder
Jennifer Jones
Beth Kearney
Joy Olea

Amber Pelland
Todd Rigby
Hugo Villanueva
Amanda Wade

CNUSD Staff Members

Michael Lin, Ed.D., Superintendent

Sam Buenrostro, Deputy Superintendent
Alan Giles, Assistant Superintendent
John Vondriska, Administrative Director

Troy Shaddox, Director II
Nancy Baker, Director I
Vanessa Dingler, Secretary

AGENDA

1. **CALL TO ORDER**
2. **PLEDGE OF ALLEGIANCE**
3. **PUBLIC COMMENT**
4. **OVERSIGHT COMMITTEE ACTIONS**
 - a. Adoption of Minutes – February 3, 2020
5. **CNUSD UPDATES**
 - a. GO Bond Refunding by Tim Carty, Piper Sandler & Co.
 - b. C.O.C. Purpose and Composition, Alan P. Giles
 - c. Projects Update Presentation by John C. Vondriska
6. **OTHER ITEMS**
 - a. Annual Report to the Board of Education – December 15, 2020
 - b. Future meeting dates
 - November 30, 2020
 - February 22, 2021
 - May 24, 2021

For **PUBLIC COMMENT**, please email any comments to vdingler@cnusd.k12.ca.us by no later than 12:00 p.m. on August 24, 2020. In the email Subject line include the following: PUBLIC COMMENT and the Section of the agenda you wish to address. The submissions will be read aloud during the meeting. The meeting will be recorded and will be posted on the CNUSD website the following day.

**CORONA-NORCO UNIFIED SCHOOL DISTRICT
MEASURE GG
CITIZENS' OVERSIGHT COMMITTEE**

MEETING MINUTES

**Monday, February 3, 2020
Corona-Norco Unified School District
Board Room**

ATTENDEES

Committee Members:

- | | | |
|--|--|---|
| <input type="checkbox"/> Nilo Ambriz | <input type="checkbox"/> Kevin Bash | <input checked="" type="checkbox"/> Gregory Coker |
| <input type="checkbox"/> Raul Gomez | <input type="checkbox"/> Bryan Graves | <input type="checkbox"/> Corinne Holder |
| <input checked="" type="checkbox"/> Jennifer Jones | <input checked="" type="checkbox"/> Beth Kearney | <input checked="" type="checkbox"/> Jami Merchant |
| <input checked="" type="checkbox"/> Joy Olea | <input checked="" type="checkbox"/> Todd Rigby | <input checked="" type="checkbox"/> Hugo Villanueva |
| <input checked="" type="checkbox"/> Amanda Wade | | |

District Staff/Board Members:

- | | | |
|---|--|---|
| <input checked="" type="checkbox"/> Sam Buenrostro | <input checked="" type="checkbox"/> Alan Giles | <input checked="" type="checkbox"/> Ben Odipo |
| <input checked="" type="checkbox"/> John Vondriska | <input checked="" type="checkbox"/> Troy Shaddox | <input checked="" type="checkbox"/> Nancy Baker |
| <input checked="" type="checkbox"/> Vanessa Dingler | | |

1. CALL TO ORDER

The meeting was called to order at 6:30 pm.

2. PLEDGE OF ALLEGIANCE

Gregory Coker led the Pledge of Allegiance.

3. PUBLIC COMMENT

No public comment was made.

4. OVERSIGHT COMMITTEE ACTIONS

a) Adoption of Meeting Minutes – October 21, 2019

Beth Kearney made a motion to approve the minutes with the corrections requested; Jennifer Jones seconded the motion and the committee agreed to approve the meeting minutes.

Corrections were made to sections 6.b. – revise the Annual Report Date to reflect June 2018 – July 2019 and Section 3. – Second to last sentence to reflect comment was made by Mr. Morgan.

b) Adoption of Meeting Minutes – December 10, 2019, Special Meeting

Beth Kearney made a motion to approve the minutes; Jami Merchant seconded the motion and the committee agreed to approve the meeting minutes.

5. AUDIT REPORT

By Andrew Park, Eide Bailly, LLP.

Andrew Park presented the Measure GG Bond Audit Report for the period of July 1, 2018 through June 30, 2019. Mr. Park explained that his firm recently changed its name from Vavrinek, Trine & Day (VTD) to Eide Bailly.

**CORONA-NORCO UNIFIED SCHOOL DISTRICT
MEASURE GG
CITIZENS' OVERSIGHT COMMITTEE**

Mr. Park briefly explained the Balance sheet and the Income Statement sheet on pages 3 and 4 of the audit report. He reminded committee members that the purpose of the audit is to confirm that the numbers reported are correct. Mr. Park stated that after auditing the numbers, the numbers in the report are true.

He reminded committee members that the bond audit report is composed of two separate components. The first part consists of the Financial Statement and the second part consists of the Performance/Compliance Audit. The second part of the report relates to how the money is being spent and if it is in accordance to what voters have approved for Measure GG.

Mr. Park stated that 49 transactions were audited, covering approximately \$57.9 million which represents 83% of the total expenditures. Based on the audit performed, the auditors did not identify any expenditures outside of the approved ballot measures. He explained that the principal behind auditing is based on random sampling and although only 49 transactions were audited, this equates to 83% of the total bond which is significant.

He explained that the audit is a process designed to provide reasonable reassurance that the financial statements are free of mistakes and this is done by providing an opinion. The highest level of assurance is considered a clean opinion. Mr. Park stated that a clean opinion was issued for the use of the Measure GG funds. He mentioned that if he would have found any discrepancies, he would have issued a modified opinion and he stated that that is not the case for Measure GG.

6. COMMUNICATIONS UPDATE

By Brittany Foust, Communications Manager

Brittany Foust shared the latest winter video including the Measure GG updates that has been shared with the community via the CNUSD website and YouTube Channel. Another video will be prepared and shared with the community in the fall of 2020. In addition, other short videos, Measure GG Monday posts and the Parent CNUSD Connections Newsletter continue to reach the community members with Measure GG updates.

7. CNUSD UPDATES

a) Financial Report

John Vondriska, Administrative Director presented the Measure GG Financial Report for the committee to review. All changes have been highlighted for easy reference. He mentioned Issuance C has been added to the report.

Mr. Vondriska mentioned that for Adams Elementary School, expenditures may still be received but that any remaining funds will be used on other site projects.

A discussion ensued regarding roofing repairs. Mr. Giles also mentioned that there was a dire need for roofing repairs throughout the district and that \$7 million was allocated from Issuance C for these major roof repairs. A combination of Routine Repair Maintenance Funds and Measure GG Funds will be used to cover the cost of the major roof repairs throughout the district. As of today, we estimate that approximately \$1 million has been spent from the Routine Repair Maintenance funds and \$5 million from Measure GG funds for roofing repairs at different sites. As of this moment, Lincoln is not scheduled to receive any roofing repairs.

**CORONA-NORCO UNIFIED SCHOOL DISTRICT
MEASURE GG
CITIZENS' OVERSIGHT COMMITTEE**

A suggestion was made to inform the committee members of any changes/updates to the project list in advance and not after the changes have occurred. Perhaps at future meetings, district administrators could make information available on items that the district is considering that are not currently listed on the project list.

At Foothill Elementary, the project consisted of the removal of nine old relays that are not currently in use. Replacements will not occur until the next issuance of the bond. The plan is to clean up the area and leave a dirt area until the next issuance.

For Garretson Elementary, the overage of \$97,000 listed in the report came from Lincoln Fundamental. For Lincoln Fundamental, a change in the expenditures occurred. Nothing new was added to the project site, but expenditures were received that were pending. For Santiago High School, under the fencing project, the overage listed will be moved to another Measure GG Project in Corona.

A comment was made in regards to the Measure GG Funds in the Eastvale area. On the report, approximately \$1 million in Measure GG funds were spent on roof repairs at Clara Barton Elementary and Roosevelt High School; but the Eastvale area has already exceeded the amount allocated for them bringing Eastvale to approximately \$32 million over what was allocated in bond language. Mr. Giles reminded committee members that once state funds are received, these will be used to cover any overages spent in the Eastvale area. At the end of the bond, all areas will receive their allocated amount per bond language. As of this moment, the district is approved and expects to receive approximately \$38 million from Prop 51 which is the \$9 billion State Facility Bond. The timeline is not known at this moment. Mr. Vondriska explained the process of applying for these Prop 51 State funds and explained Prop 13 that will be on the ballot in March.

A concern was expressed that if these state funds were not received, pending projects on the list would not be completed. Community members are worried that areas such as Norco will not receive enough funds to complete necessary projects at the sites, including shade structures that are needed since old trees are rotting and falling down. Committee members mentioned that the community perception is that Eastvale has received more money for projects and other areas have not received the funding for necessary upgrades. District Administrators are constantly looking at ways to save money and applying for any possible State reimbursements.

Expenditures at Norco Intermediate have increased. Current expenditures at Norco Intermediate are at \$6.6 million and \$14.4 million has been added to this project for the next issuance.

Troy Shaddox, IT Director, presented the Information Technology section of the Financial Report. All changes on the report have been highlighted for easy reference. He explained that the priority of Issuance A and B are technology updates to the classrooms, such as projectors, control systems, speakers, etc.

Corona Fundamental is complete with classroom technology updates. Funds are still available for future infrastructure and cabling updates at CFIS. At the end of Issuance B, all classrooms within the district will have updated classroom technology. Technology purchases were decided by the Ed Tech Committee at CNUSD and not by individual sites.

For Issuance C, Information Technology will receive \$7.5 million and the plan is to use this for infrastructure such as network switches at school sites, data drops per classrooms, etc. The plan with Issuance C and D is to provide up to 9 data drops per classroom.

**CORONA-NORCO UNIFIED SCHOOL DISTRICT
MEASURE GG
CITIZENS' OVERSIGHT COMMITTEE**

Limited funds are being used for cabling at this moment, most of the funds are used for classrooms technology updates. Technology training has been offered to teachers and there are Site Champions at each school site who can provide further training if needed. Additional training from Educational Services and Ed Tech is provided to teachers if needed.

b) Project List Update

John Vondriska, Administrative Director, presented the project list. All changes have been highlighted for easy reference. Many of the changes on the report reflect the Information Technology updates and will be listed as in progress. These will not be listed as finalized until closer to the end since all sites will be revisited to complete other items such as switches or interactive whiteboards, etc. No school site as of this moment is 100% complete in regards to technology updates.

For Corona Fundamental, the Job Walk is scheduled this week and the Architect selection process will begin. After the Architect is selected, the Contractor selection process will begin. Once the drawings/plan are prepared, they will be submitted to DSA (Division of State Architect) for approval. This process can usually take between 12-14 months. Administrators will ensure that this project does not exceed the budget allocated. For the CFIS project, we will maintain the historical structure throughout.

In regards to Neff Construction, the last project they were awarded was Rondo School of Discovery and they have not placed a bid for any other CNUSD project. The District is currently with Erickson Hall and West Coast Air as general contractors.

8. OTHER ITEMS

a) Bylaw Revision 6.1

In reviewing the Bylaws, under section 6.1 Regular Meetings, it is stated that an annual organizational meeting is to be held every year in July. Since the committee does not meet during the month of July, District Administrators recommend we remove the month of July and only state that an annual organizational meeting is to be held each year. If COC members approve of this change, the amended bylaws will be taken to the Board of Education on March 3 for approval.

Todd Rigby made a motion to approve the amended bylaws with the correction requested; Jami Merchant seconded the motion and the committee agreed to approve the amended bylaws.

b) Member Terms

Committee members were provided with a copy of the updated Member List. Three COC members' terms expire in February this year. Hugo Villanueva, Jami Merchant and Kevin Bash are all eligible for another term. Per the recommendation of David Soldani, attorney with AALRR, 3 year terms were issued with the purpose of staggering terms, but moving forward, all new terms will be 2-year terms.

Hugo Villanueva and Jami Merchant have agreed to another 2-year term. Kevin Bash will be contacted by district staff. The new terms will be taken to the Board of Education on March 3 for approval.

The meeting was adjourned at 8:03 p.m.



Measure
GG

Citizens'
Oversight
Committee

ANNUAL REPORT

July 2018 - June 2019

HISTORY

In accordance with 2014-2015 Resolution No. 40, approved by the Corona-Norco Unified School District Board of Education on August 5, 2014, the Board is committed to maintaining the quality of education in local schools with safe, upgraded classrooms, libraries, science labs and technology systems to keep pace with 21st century learning standards. To that end, the Board evaluated the District's urgent and critical facility needs, including safety issues, class size, computer and information technology, enrollment trends and prepared a Master Facilities Plan in developing the scope of projects to be funded. Based on the results of this evaluation, it was determined that the Measure GG bond funds were to be equitably distributed between projects benefitting the areas of Corona, Norco and Eastvale based on each area's assessed valuation at the time the bond initiative was being prepared. As a result, Corona is to receive 63% of the bond funds, Norco 14% of the bond funds and Eastvale 23% of the bond funds. The allocation of bond proceeds used to fund projects listed on the scope of projects may be affected by the District's receipt of State matching funds and the final costs of each project. In the absence of State matching funds, which the District will aggressively pursue to reduce the District's share of the costs of the projects, the District may not be able to complete some of the projects listed. The budget for each project is an estimate and may be affected by factors beyond the District's control. The final cost of each project will be determined as plans are finalized, construction bids are awarded and projects are completed. Based on the final costs of each project, certain projects listed on the scope of projects may be delayed or may not be completed.

Proceeds from the sale of the bonds shall be used only for the acquisition, construction, reconstruction, rehabilitation, or replacement of school facilities, including the furnishing and equipping of school facilities, and not for any other purpose, including teacher and school administrator salaries and other operating expenses.



*Corona/Unincorporated communities include: Coronita, El Cerrito, Home Gardens, and Temescal Valley
**Eastvale includes Jurupa Valley



CITIZENS' OVERSIGHT COMMITTEE

Measure GG is a \$396 million bond that authorizes funding for needed repairs, upgrades, and new construction projects. With the passage of Measure GG, the law requires a Citizens' Oversight Committee be established to assure bond funds are used as outlined in the ballot. The Citizens' Oversight Committee was formed February 2015. The committee is comprised of parents, senior citizens, business and civic leaders. We encourage all to visit the District's website for regular updates.

The passage of this bond measure creates far-reaching, positive educational opportunities for our students of today and for generations to come. As a school district, we will roll up our sleeves and go about the work we have always done - to create hope, opportunity, and a better future for all students.

PURPOSE

- Inform the public concerning the expenditure of bond revenues
- Actively review and report on the proper expenditure of taxpayers' money for school construction
- Advise the public as to whether the district is in compliance with the requirements of Proposition 39

RESPONSIBILITIES

- Ensure all committee proceedings are open to the public
- Issue regular activity reports and an annual report to CNUSD Board of Education
- Ensure all minutes of meetings, documents received and reports issued are made public and are available on the district (CNUSD) website

Citizens' Oversight Committee Members

NAME	CATEGORY	CITY REPRESENTING
Gregory Coker, CHAIR	At-Large Community	Eastvale
Jami Merchant, VICE CHAIR	At-Large Community	Corona/Unincorporated
Corinne Holder	At-Large Community	Norco
Hugo Villanueva	Tax Payer Organization	Corona/Unincorporated
Beth Kearney	Senior Citizen Representative	Corona/Unincorporated
Bryan Graves	Business Representative	Corona/Unincorporated
Kevin Bash	Business Representative	Norco
Todd Rigby	Business Representative	Eastvale
Nilo Ambriz	Parent	Corona
Amanda Wade	Parent	Norco
Raul Gomez	Parent	Eastvale
<i>Vacancy</i>	<i>Parent & PTA Representative</i>	<i>Corona/Unincorporated</i>
Joy Olea	Parent & PTA Representative	Norco
Jennifer Jones	Parent & PTA Representative	Eastvale



Measure GG Projects

CORONA/UNINCORPORATED

Completed Measure GG modernization projects in the Corona/Unincorporated area are: **Adams Elementary, Garretson Elementary, and Lincoln Fundamental Elementary School.**



Measure GG Projects

CORONA/UNINCORPORATED



The Construction and Modernization project at **Jefferson Elementary School** started in the Summer of 2019. The project is slated to include a new administrative building, new library, new computer lab, and new classrooms. The estimated completion date is Summer of 2021.



Measure GG Projects

NORCO

The Measure GG modernization project **Norco Elementary School** is complete. The project included a new administrative building, new library/media center, new multi-purpose room (MPR), refurbished kinder classrooms, a new shade shelter and an improved parking lot.

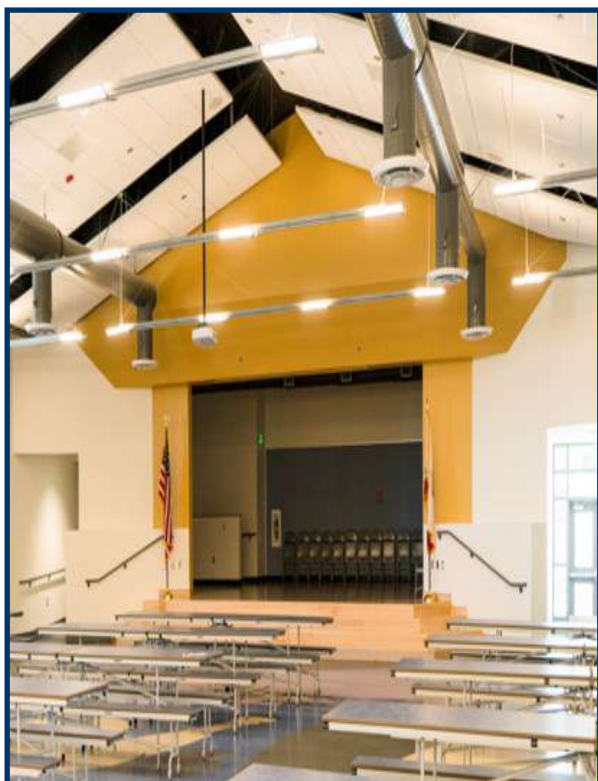

Measure GG Projects

NORCO

Construction of the Measure GG modernization project at **Norco Intermediate School** started in the Summer of 2019.



This project will include a new administrative building, new library, new multi-purpose room/gymnasium, and an improved parking lot to help with traffic flow in and around the school. The estimated completion date for this modernization project is the Summer of 2021.



Measure GG Projects

EASTVALE

Construction of the new **eSTEM High School** located on the Roosevelt High School campus is complete and the school opened on August 12, 2019 for the 2019-2020 school year. Updates to the student parking lot adjacent to Citrus Street were completed in time for the start of the new school year.



A second project in Eastvale as part of Measure GG is the **Rondo School of Discovery**. Construction for this school started in November of 2017 and is currently scheduled to be completed by December 2019. The proposed opening for this site is July of 2020 for the 2020-21 multi-track school year.



Measure GG Projects

INFORMATION TECHNOLOGY

Technology updates have been part of Measure GG funding. The Measure GG Technology funding is focused on *Infrastructure* and *Classroom Technology*. The infrastructure includes data pathways, cabling, and electrical infrastructure. The classroom technology includes a complete control system that unifies the classroom digital learning environment. A total of \$60 million will be used for technology.

A total of \$30 million has been allocated towards the above technology installs and upgrades across the district. Installation for classroom technology is continuing and scheduled to be complete by the end of 20\21 school year. To date, we have finalized installation of 1,300 projectors, 300 whiteboards, and over 3,000 data drops. Elementary schools received 250 interactive whiteboards. Ongoing professional development for the new technology continues to be provided to certificated staff.



MEASURE GG PROJECT LIST

The Measure GG Project List has been attached to the back of this report as an addendum for your reference reflecting the latest activity as of September 30, 2019.

Audit Summary

AUDIT

The passage of Measure GG and issuance of bonds require a school district to conduct annual independent financial and performance audits of the General Obligation Bond proceeds and expenditures. An audit was performed and disseminated to the Citizens' Oversight Committee on March 11, 2019 in accordance with Government Code Section 15278.

The results of the audit indicated that Corona-Norco Unified School District has properly accounted for the expenditures held in the Measure GG fund and that such expenditures were made for authorized bond projects.

The full audit report is available on the CNUSD Website, under Measure GG.

After careful review, the Citizens' Oversight Committee finds all funds were expended appropriately for purposes stated in Measure GG, and has determined that based upon these records, none of the expenditures were used for teacher salaries, administrative costs or other operating expenses. The Citizens' Oversight Committee concluded that the District is in compliance with Proposition 39.

Financial Summary

FINANCIAL

Issue A Proceeds Received July 2015

Issue B Proceeds Received April 2018


	PROCEEDS	INCOME	AUDITED EXPENDITURES THRU JUNE 30, 2018	UNAUDITED EXPENDITURES THRU JUNE 30, 2019	REMAINING
Corona/ Unincorporated	\$84,322,530	\$1,617,803	\$56,082,830	\$4,301,589	\$25,555,914
Eastvale	\$76,250,000		\$38,147,137	\$60,412,722	(\$22,309,859)
Norco	\$27,506,932		\$17,792,945	\$1,956,653	\$7,757,334
Information	\$30,000,000	\$664,408	\$16,917,266	\$2,789,166	\$10,957,975
Total	\$218,079,462	\$2,282,211	\$128,940,178	\$69,460,130	\$21,961,364

Community Outreach

A comprehensive community outreach program has been developed to ensure that residents in the Corona -Norco Unified School District service area are updated on the progress of Measure GG projects. Included in the plan are strategies and tools that will be utilized to reach the community. The communication's plan includes the utilization of social media, banners, videos, interactive website, community meeting presentations and e-newsletter stories. A sampling of some of those strategies can be found below.

SOCIAL MEDIA OUTREACH

Consistent and strategic social media posting about the Measure GG construction progress including photos and videos. #MeasureGGMonday is a campaign that has included consistent photo and video releases that highlight the projects that are currently under way or completed utilizing Measure GG funding.

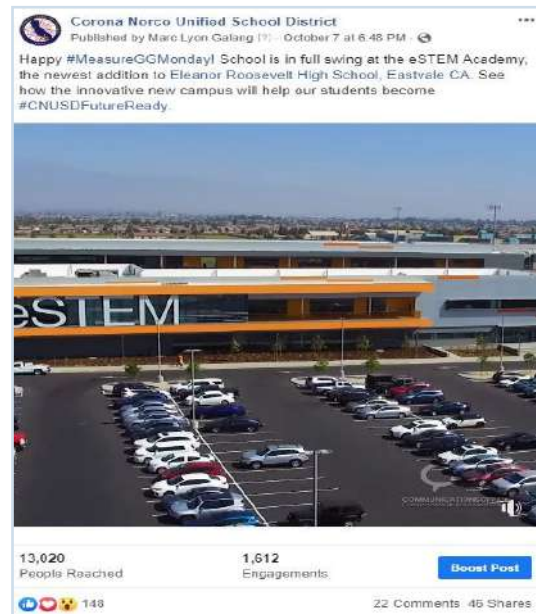

VIDEOS


Keeping the community informed about the progress of Measure GG Projects includes the use of video. A video series called, "Measure GG Community Updates" was launched in 2016 and continues to highlight the progress of our Measure GG projects throughout the district. The first video was released the summer of 2016. These videos are shared on social media and the CNUSD Connection e-newsletter. The next scheduled update will be the Fall 2019.



Community Outreach

WEBSITE UPDATES

The District website has a landing page specifically for all Measure GG information. The community has access to all information pertaining to the Measure GG Citizen’s Oversight Committee, agendas and minutes, construction updates, as well as the latest Measure GG Update videos.



RIBBON CUTTING EVENTS

In celebration of the opening of our new facilities the following Ribbon Cuttings are planned to celebrate with the community.

The Ribbon Cutting event for Roosevelt eSTEM was held on November 8, 2019.

Philistine Rondo School of Discovery: TBD





For More Information Visit:
www.cnusd.k12.ca.us

Corona-Norco Unified School District
2820 Clark Avenue
Norco, CA 92860

**Measure GG Project List
As of Sept 30, 2019**

SCHOOL	AREA	PROJECTED BUDGET Includes other sources	MEASURE GG FUNDS	PROJECT STATUS	PROJECT NOTES	RESPONSIBLE DIVISION
ADAMS ELEMENTARY	Corona	19,325,113	19,325,113	COMPLETE	Project at 100% Complete	FACILITIES
		87,500	87,500	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
ANTHONY ELEMENTARY	Corona	99,655	10,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		207,116	207,116	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
BERNICE TODD ACADEMY	Corona	165,478	165,478	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
CORONA RANCH ELEMENTARY	Corona	91,597	91,597	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
CORONITA ELEMENTARY	Corona	257,303	257,303	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
EISENHOWER ELEMENTARY	Corona	376,231	376,231	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY

ADDENDUM

**Measure GG Project List
As of Sept 30, 2019**

SCHOOL	AREA	PROJECTED BUDGET Includes other sources	MEASURE GG FUNDS	PROJECT STATUS	PROJECT NOTES	RESPONSIBLE DIVISION
FOOTHILL ELEMENTARY	Corona	175,000	175,000	COMPLETE	Fencing Upgrades. Project 100% complete.	FACILITIES
		722,993	722,993	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
FRANKLIN ELEMENTARY	Corona	55,624	10,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		51,970	51,970	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
GARRETSON ELEMENTARY	Corona	20,010,775	20,010,775	COMPLETE	Project at 100% Complete	FACILITIES
		672,054	672,054	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards, Network equipment	INFORMATION TECHNOLOGY
JEFFERSON ELEMENTARY	Corona	179,259	125,000	TBD	Fencing Upgrades	SUPPORT SERVICES
		24,778,750	24,778,750	IN PROGRESS	Admin/Library/classrooms. 12% complete.	FACILITIES
		123,410	123,410	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
LINCOLN ALTERNATIVE ELEM	Corona	18,225,428	18,225,428	COMPLETE	Project at 100% Complete	FACILITIES
		528,353	528,353	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY

**Measure GG Project List
As of Sept 30, 2019**

SCHOOL	AREA	PROJECTED BUDGET Includes other sources	MEASURE GG FUNDS	PROJECT STATUS	PROJECT NOTES	RESPONSIBLE DIVISION
MCKINLEY ELEMENTARY	Corona	9,406	9,406	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		72,146	72,146	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
ORANGE ELEMENTARY	Corona	566,964	566,964	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards, Network equipment.	INFORMATION TECHNOLOGY
PARKRIDGE ELEMENTARY	Corona	329,862	329,862	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
PRADO VIEW ELEMENTARY	Corona	315,901	25,000	COMPLETE	KG Fencing	SUPPORT SERVICES
		253,280	253,280	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards.	INFORMATION TECHNOLOGY
STALLINGS ELEMENTARY	Corona	151,105	85,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		238,231	238,231	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards.	INFORMATION TECHNOLOGY

**Measure GG Project List
As of Sept 30, 2019**

SCHOOL	AREA	PROJECTED BUDGET Includes other sources	MEASURE GG FUNDS	PROJECT STATUS	PROJECT NOTES	RESPONSIBLE DIVISION		
TEMESCAL VALLEY ELEMENTARY	Corona	394,600	394,600	COMPLETE	†Security Cameras	SUPPORT SERVICES		
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards.	INFORMATION TECHNOLOGY		
VICENTIA ELEMENTARY	Corona	79,967	79,967	COMPLETE	†Security Cameras	SUPPORT SERVICES		
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY		
WASHINGTON ELEMENTARY	Corona	239,105	168,935	COMPLETE	Fencing Upgrades	SUPPORT SERVICES		
				353,181	353,181	COMPLETE	†Security Cameras	SUPPORT SERVICES
						IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
WILSON ELEMENTARY	Corona	341,587	341,587	COMPLETE	†Security Cameras	SUPPORT SERVICES		
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY		
VICTRESS BOWER	Corona	155,055	90,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES		
				100,007	100,007	COMPLETE	†Security Cameras	SUPPORT SERVICES
						IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards.	INFORMATION TECHNOLOGY

**Measure GG Project List
As of Sept 30, 2019**

SCHOOL	AREA	PROJECTED BUDGET Includes other sources	MEASURE GG FUNDS	PROJECT STATUS	PROJECT NOTES	RESPONSIBLE DIVISION
AUBURNDALE INTERMEDIATE	Corona	436,391	305,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		429,951	429,951	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
CHAVEZ ACADEMY K-8	Corona	1,857,224	1,200,000	COMPLETE	Dirt Track, Natural Grass Field, Play Structure	FACILITIES
		375,937	375,937	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
CITRUS HILLS INTERMEDIATE	Corona	720,985	720,985	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
CORONA FUNDAMENTAL INTERM	Corona	182,131	182,131	COMPLETE	Fencing Upgrades. Project 100% complete.	SUPPORT SERVICES
		93,722	93,722	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards.	INFORMATION TECHNOLOGY
EL CERRITO MIDDLE	Corona	41,528	41,528	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		103,893	103,893	COMPLETE	†Security Cameras	SUPPORT SERVICES
					Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards	INFORMATION TECHNOLOGY

**Measure GG Project List
As of Sept 30, 2019**

SCHOOL	AREA	PROJECTED BUDGET Includes other sources	MEASURE GG FUNDS	PROJECT STATUS	PROJECT NOTES	RESPONSIBLE DIVISION
HOME GARDENS ACADEMY K-8	Corona	376,460	376,460	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards.	INFORMATION TECHNOLOGY
RANEY INTERMEDIATE	Corona	560,575	325,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
				COMPLETE	†Security Cameras	SUPPORT SERVICES
		503,411	503,411	IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
CENTENNIAL HIGH	Corona	25,000	25,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
				COMPLETE	†Security Cameras	SUPPORT SERVICES
		614,156	614,156	IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Pull Down Screens	INFORMATION TECHNOLOGY
CORONA HIGH	Corona	95,000	95,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
				COMPLETE	†Security Cameras	SUPPORT SERVICES
		1,777,266	1,777,266	IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Pull Down Screens, Network Equipment	INFORMATION TECHNOLOGY
ORANGE GROVE HIGH	Corona	236,977	100,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
				COMPLETE	†Security Cameras	INFORMATION TECHNOLOGY
		367,148	367,148	IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards	INFORMATION TECHNOLOGY

**Measure GG Project List
As of Sept 30, 2019**

SCHOOL	AREA	PROJECTED BUDGET Includes other sources	MEASURE GG FUNDS	PROJECT STATUS	PROJECT NOTES	RESPONSIBLE DIVISION
LEE POLLARD HIGH	Corona	45,596	45,596	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Pull Down Screens	INFORMATION TECHNOLOGY
SANTIAGO HIGH	Corona	700,000	700,000	COMPLETE	HVAC upgrade	SUPPORT SERVICES
				COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		1,099,470	1,099,470	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Pull Down Screens	INFORMATION TECHNOLOGY
BARTON ELEMENTARY	Eastvale	368,487	368,487	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
EASTVALE ELEMENTARY	Eastvale	306,101	306,101	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
HARADA ELEMENTARY	Eastvale	389,623	389,623	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards, Network equipment	INFORMATION TECHNOLOGY
LOUIS VANDERMOLLEN ELEMENTARY	Eastvale	22,744	22,744	COMPLETE	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
				IN PROGRESS	†Security Cameras	SUPPORT SERVICES
RONALD REAGAN ELEMENTARY	Eastvale	43,524	43,524	COMPLETE	†Security Cameras (Included in site construction)	FACILITIES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY

**Measure GG Project List
As of Sept 30, 2019**

SCHOOL	AREA	PROJECTED BUDGET Includes other sources	MEASURE GG FUNDS	PROJECT STATUS	PROJECT NOTES	RESPONSIBLE DIVISION
ROSA PARKS ELEMENTARY	Eastvale	213,945	213,945	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
PHILISTINE RONDO ELEMENTARY	Eastvale	54,784,694	20,000,000	COMPLETE	PHASE I - SITE WORK 100% Complete	FACILITIES
				IN PROGRESS	PHASE 2 - CAMPUS 85% Complete	
RAMIREZ INTERMEDIATE	Eastvale	68,191	68,191	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards.	INFORMATION TECHNOLOGY
RIVER HEIGHTS INTERMEDIATE	Eastvale	379,870	379,870	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards	INFORMATION TECHNOLOGY
ROOSEVELT HIGH	Eastvale	1,218,937	1,218,937	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Pull Down Screens.	INFORMATION TECHNOLOGY
ROOSEVELT HIGH	Eastvale	750,000	750,000	COMPLETE	Upgrades	FACILITIES
ROOSEVELT HIGH eSTEM	Eastvale	70,101,270	55,500,000	COMPLETE	PHASE 1, 1A & 2 - Project 100% Complete	FACILITIES
				IN PROGRESS	PHASE 2A & 2B - Project approximately 98% Complete	

**Measure GG Project List
As of Sept 30, 2019**

SCHOOL	AREA	PROJECTED BUDGET Includes other sources	MEASURE GG FUNDS	PROJECT STATUS	PROJECT NOTES	RESPONSIBLE DIVISION
HIGHLAND ELEMENTARY	Norco	178,893	75,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		391,267	391,267	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards.	INFORMATION TECHNOLOGY
NORCO ELEMENTARY	Norco	18,843,768	18,843,768	COMPLETE	Project at 100% Complete	FACILITIES
		190,074	190,074	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
RIVERVIEW ELEMENTARY	Norco	204,977	100,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		182,163	182,163	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards	INFORMATION TECHNOLOGY
SIERRA VISTA ELEMENTARY	Norco	199,358	150,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		54,992	54,992	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Interactive Whiteboards.	INFORMATION TECHNOLOGY

**Measure GG Project List
As of Sept 30, 2019**

SCHOOL	AREA	PROJECTED BUDGET Includes other sources	MEASURE GG FUNDS	PROJECT STATUS	PROJECT NOTES	RESPONSIBLE DIVISION
NORCO INTERMEDIATE	Norco	300,000	300,000	TBD	Fencing Upgrades	SUPPORT SERVICES
		7,938,164	7,938,164	IN PROGRESS	School Upgrades 12% complete.	FACILITIES
		552,547	552,547	COMPLETE	†Security Cameras	SUPPORT SERVICES
IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards			INFORMATION TECHNOLOGY		
JOHN F KENNEDY HIGH	Norco	132,594	132,594	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards	INFORMATION TECHNOLOGY
NORCO HIGH	Norco	223,193	100,000	COMPLETE	Fencing Upgrades	SUPPORT SERVICES
		849,448	849,448	COMPLETE	†Security Cameras	SUPPORT SERVICES
				IN PROGRESS	Classroom drops, Projectors/Speakers/Wall mounts, Whiteboards, Pull Down Screens	INFORMATION TECHNOLOGY
Unallocated Technology		10,342,294	10,342,294	COMPLETE		INFORMATION TECHNOLOGY
DISTRICT OFFICE Technology	District	2,435,780	2,435,780	TBD	VDI, Servers, Data Storage, Personalized Learning, Data Center upgrades, Video Surveillance Infrastructure, Security Cameras	INFORMATION TECHNOLOGY
		272,088,727	220,478,406			

Measure GG

Citizens' Oversight Committee

ANNUAL REPORT PRESENTATION

December 17, 2019



CORONA-NORCO UNIFIED SCHOOL DISTRICT

Measure GG History

In accordance with 2014-2015 Resolution No. 40, approved by the Corona-Norco Unified School District Board of Education on August 5, 2014, the Board is committed to maintaining the quality of education in local schools with safe, upgraded classrooms, libraries, science labs and technology systems to keep pace with 21st century learning standards. To that end, the Board evaluated the District's urgent and critical facility needs, including safety issues, class size, computer and information technology, enrollment trends and prepared a Master Facilities Plan in developing the scope of projects to be funded. Based on the results of this evaluation, it was determined that the Measure GG bond funds were to be equitably distributed between projects benefitting the areas of Corona, Norco and Eastvale based on each area's assessed valuation at the time the bond initiative was being prepared. As a result, Corona is to receive 63% of the bond funds, Norco 14% of the bond funds and Eastvale 23% of the bond funds. The allocation of bond proceeds used to fund projects listed on the scope of projects may be affected by the District's receipt of State matching funds and the final costs of each project. In the absence of State matching funds, which the District will aggressively pursue to reduce the District's share of the costs of the projects, the District may not be able to complete some of the projects listed. The budget for each project is an estimate and may be affected by factors beyond the District's control. The final cost of each project will be determined as plans are finalized, construction bids are awarded and projects are completed. Based on the final costs of each project, certain projects listed on the scope of projects may be delayed or may not be completed.

Proceeds from the sale of the bonds shall be used only for the acquisition, construction, reconstruction, rehabilitation, or replacement of school facilities, including the furnishing and equipping of school facilities, and not for any other purpose, including teacher and school administrator salaries and other operating expenses.

Measure GG

Citizens' Oversight Committee

Measure GG is a \$396 million bond that authorizes funding for needed repairs, upgrades, and new construction projects. As a requirement, the Citizens' Oversight Committee was established in February 2015 to ensure bond funds are used as outlined in the ballot. The committee is composed of parents, senior citizens, business and civic leaders.

PURPOSE:

- Inform the public concerning the expenditure of bond revenues
- Actively review and report on the proper expenditures of taxpayers' money for school construction
- Advise the public as to whether the district is in compliance with the requirements with Proposition 39

RESPONSIBILITIES:

- Ensure all committee proceedings are open to the public
- Issue regular activity reports and an annual report to CNUSD Board of Education
- Ensure all minutes of meetings, documents received and reports issued are made public and are available on the district (CNUSD) website



Measure GG Citizens' Oversight Committee Members

NAME	CATEGORY	CITY REPRESENTING
Gregory Coker, CHAIR	At-Large Community	Eastvale
Jami Merchant, VICE CHAIR	At-Large Community	Corona/Unincorporated
Corinne Holder	At-Large Community	Norco
Hugo Villanueva	Tax Payer Organization	Corona/Unincorporated
Beth Kearney	Senior Citizen Representative	Corona/Unincorporated
Bryan Graves	Business Representative	Corona/Unincorporated
Kevin Bash	Business Representative	Norco
Todd Rigby	Business Representative	Eastvale
Nilo Ambriz	Parent	Corona
Amanda Wade	Parent	Norco
Raul Gomez	Parent	Eastvale
<i>Vacancy</i>	<i>Parent & PTA Representative</i>	<i>Corona/Unincorporated</i>
Joy Olea	Parent & PTA Representative	Norco
Jennifer Jones	Parent & PTA Representative	Eastvale



Measure GG Projects in Corona/Unincorporated

CORONA/UNINCORPORATED

Completed Measure GG modernization projects in the Corona/Unincorporated area are: **Adams Elementary, Garretson Elementary, and Lincoln Fundamental Elementary School.**



Measure GG Projects in Corona/Unincorporated

CORONA/UNINCORPORATED

The Construction and Modernization project at **Jefferson Elementary School** started in the Summer of 2019. The project is slated to include a new administrative building, new library, new computer lab, and new classrooms. The estimated completion date is Summer of 2021.



Measure GG Projects in Norco

NORCO

The Measure GG modernization project **Norco Elementary School** is complete. The project included a new administrative building, new library/media center, new multi-purpose room (MPR), refurbished kinder classrooms, a new shade shelter and an improved parking lot.



Measure GG Projects in Norco

NORCO

Construction of the Measure GG modernization project at **Norco Intermediate School** started in the Summer of 2019. This project will include a new administrative building, new library, new multi-purpose room/gymnasium, and an improved parking lot to help with traffic flow in and around the school. The estimated completion date for this modernization project is the Summer of 2021.



Measure GG Projects in Eastvale

EASTVALE

Construction of the new **eSTEM High School** located on the Roosevelt High School campus is complete and the school opened on August 12, 2019 for the 2019-2020 school year. Updates to the student parking lot adjacent to Citrus Street were completed in time for the start of the new school year.

A second project in Eastvale as part of Measure GG is the **Rondo School of Discovery**. Construction for this school started in November of 2017 and is currently scheduled to be completed by December 2019. The proposed opening for this site is July of 2020 for the 2020-21 multi-track school year.




Measure GG Information Technology

INFORMATION TECHNOLOGY

Technology updates have been part of Measure GG funding. The Measure GG Technology funding is focused on *Infrastructure* and *Classroom Technology*. The infrastructure includes data pathways, cabling, and electrical infrastructure. The classroom technology includes a complete control system that unifies the classroom digital learning environment. A total of \$60 million will be used for technology.

A total of \$30 million has been allocated towards the above technology installs and upgrades across the district. Installation for classroom technology is continuing and scheduled to be complete by the end of 20\21 school year. To date, we have finalized installation of 1,300 projectors, 300 whiteboards, and over 3,000 data drops. Elementary schools received 250 interactive whiteboards.

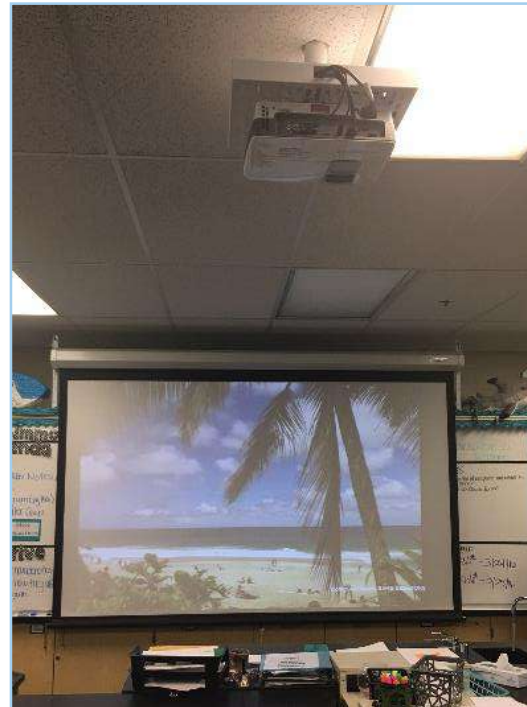

Measure GG Audit Summary

AUDIT

The passage of Measure GG and issuance of bonds require a school district to conduct annual independent financial and performance audits of the General Obligation Bond proceeds and expenditures. An audit was performed and disseminated to the Citizens' Oversight Committee on March 11, 2019 in accordance with Government Code Section 15278.

The results of the audit indicated that Corona-Norco Unified School District has properly accounted for the expenditures held in the Measure GG fund and that such expenditures were made for authorized bond projects.

The full audit report is available on the CNUSD Website, under Measure GG.

After careful review, the Citizens' Oversight Committee finds all funds were expended appropriately for purposes stated in Measure GG, and has determined that based upon these records, none of the expenditures were used for teacher salaries, administrative costs or other operating expenses. The Citizens' Oversight Committee concluded that the District is in compliance with Proposition 39.

Measure GG Financial Information

Issue A Proceeds Received July 2015

Issue B Proceeds Received April 2018

	PROCEEDS	INCOME	AUDITED EXPENDITURES THRU JUNE 30, 2018	UNAUDITED EXPENDITURES THRU JUNE 30, 2019	REMAINING
Corona/ Unincorporated	\$84,322,530	\$1,617,803	\$56,082,830	\$4,301,589	\$25,555,914
Eastvale	\$76,250,000		\$38,147,137	\$60,412,722	(\$22,309,859)
Norco	\$27,506,932		\$17,792,945	\$1,956,653	\$7,757,334
Information Technology	\$30,000,000	\$664,408	\$16,917,266	\$2,789,166	\$10,957,975
Total	\$218,079,462	\$2,282,211	\$128,940,178	\$69,460,130	\$21,961,364



Measure GG Outreach



A comprehensive community outreach program has been developed to ensure that residents in the Corona-Norco Unified School District service area are updated on the progress of Measure GG projects. Included in the plan are strategies and tools that will be utilized to reach the community. Some of those strategies include:

- ❑ **SOCIAL MEDIA OUTREACH**

#MeasureGGMonday is a campaign that has included consistent photo and video releases that highlight the projects that are currently under way or completed utilizing Measure GG funding.

- ❑ **VIDEOS**

A video series called, “Measure GG Community Updates” was launched in 2016 and continues to highlight the progress of our Measure GG projects throughout the district. These videos are shared on social media and the CNUSD Connection e-newsletter.

- ❑ **WEBSITE**

The District website has a landing page specifically for all Measure GG information. The community has access to all information pertaining to the Measure GG Citizen’s Oversight Committee, agendas and minutes, construction updates, as well as the latest Measure GG Update videos.

- ❑ **RIBBON CUTTING EVENTS**

Ribbon Cuttings are planned to celebrate with the community. The Ribbon Cutting event for Roosevelt eSTEM was held on November 8, 2019.

Thank you for your attention



**Measure GG
Citizens' Oversight Committee**

COC Contact/Term Information

NAME	CATEGORY	CITY REPRESENTING	TERM	CURRENT TERM DATES
Hugo Villanueva	Tax Payer Organization	Corona	2 year	March 3, 2020 to March 3, 2022
Beth Kearney	Senior Citizen Rep	Corona	2 year	February 19, 2019 to February 19, 2021
Jami Merchant	At-Large Community	Corona	2 year	March 3, 2020 to March 3, 2022
Gregory Coker	At-Large Community	Eastvale	3 year	February 6, 2018 to February 6, 2021
Corinne Holder	At-Large Community	Norco	3 year	February 19, 2019 to February 19, 2022
Bryan Graves	Business Rep	Corona	3 year	April 16, 2019 to April 16, 2022
Todd Rigby	Business Rep	Eastvale	3 year	February 6, 2018 to February 6, 2021
Kevin Bash	Business Rep	Norco	2 year	March 3, 2020 to March 3, 2022
Nilo Ambriz	Parent	Corona	3 year	April 16, 2019 to April 16, 2022
Raul Gomez	Parent	Eastvale	3 year	April 16, 2019 to April 16, 2022
Amanda Wade	Parent	Norco	2 year	April 16, 2019 to April 16, 2021
Amber Pelland	Parent & PTA Rep	Corona	2 year	March 3, 2020 to March 3, 2022
Jennifer Jones	Parent & PTA Rep	Eastvale	3 year	April 16, 2019 to April 16, 2022
Joy Olea	Parent & PTA Rep	Norco	2 year	February 19, 2019 to February 19, 2021
